

FOR AMY LEVER

Your health record should belong to you, not to whichever clinic you last visited.

CareManager puts the patient at the center: one health record people **build and own**, that travels with them across every provider they see. This proposal is scoped to Phase 1 — the full patient experience on mobile and web, and the platform behind it — with Phase 2's engagement layer outlined at a glance for what comes next. Milestone by milestone, each one signed off before the next begins.

PREPARED FOR

Amy Lever

PREPARED BY

Mindbrowser

ENGAGEMENT

CareManager — patient platform (mobile & web) and super admin, Phase 1

STATUS

Proposal for review

This document is confidential and prepared for Amy Lever. Proposal date September 29, 2026 · Version 1.0 · Valid 30 days

CONTENTS

- | | |
|---|---|
| 01 What we propose | 02 About Mindbrowser |
| 03 The problem today, and what CareManager changes | 04 What we would build |
| 05 How the pieces connect | 06 Architecture and integrations |
| 07 Security, compliance and ownership | 08 DevOps and environments |
| 09 Phase 1 scope, by role | 10 Phase 2, at a glance |
| 11 Delivery approach and milestones | 12 How we work together |

01 What we propose

One record, owned by the patient, built as a focused Phase 1.

Records live in silos. Solo practices get left out. A patient sees seven providers and ends up with seven portals — a login for each clinic, each holding a slice of the story and none holding the whole. When they meet a new provider, they re-key the same name, the same date of birth, the same history, and hope the labs from one place make it to the next. The record follows the clinic, not the person.

CareManager flips that. People build and own one health record that travels with them — and independent, alternative-care providers can attach to it. This proposal is scoped to **Phase 1**: the patient experience on mobile and web, and the platform behind it, ready to put in front of real providers. Phase 2 — the engagement layer and admin monetization tools — is outlined at a glance in section 10, to be scoped in full once Phase 1 is underway.

What we build

The patient experience on mobile and web, the super admin platform behind it, and the security and infrastructure foundation underneath.

How we work

Two-week milestones, each a demonstrable release you sign off before the next begins. No guesses committed as fact.

What you own

Full code ownership and IP assignment on delivery, in your own cloud accounts.

02 About Mindbrowser

A healthcare-exclusive engineering partner, built for regulated work.

We build only healthcare software, for US healthcare, and we embed compliance into every phase rather than bolting it on at the end. That focus, and a bench of clinical and interoperability experts, is why founders choose us for a build that has to be secure and scalable from day one.

250+

Healthcare companies supported

200+

HIPAA-trained, FHIR-certified engineers

50+

Healthcare solution accelerators

SOC 2

Type II certified (AICPA)

Healthcare only

We build exclusively for healthcare, with deep domain subject-matter experts on the bench, including a Chief Medical Officer and HL7/FHIR SMEs.

Working with the ecosystem

Partnerships and delivery with large health systems and digital-health companies, integrating with the platforms they already run on.

Compliance-first

SOC 2 Type II, HIPAA, GDPR, and FDA-aware practices embedded through every phase, not bolted on at the end.

Standards and certifications

SOC 2 Type II

HIPAA

GDPR

ISO 27001

HL7 / FHIR

DICOM

FDA-aware

Trusted across health systems and digital-health companies, including Northwell Health, Ochsner, Nuvance Health, Northwestern, and Epic-integrated practices. Deep integration experience with Epic, Cerner, and Athena, and a founding-team heritage in telehealth (the team behind Doxy.me).

03 The problem today, and what CareManager changes

The platform is being built around this exact gap.

TODAY, WITHOUT A SHARED RECORD

- A login for every clinic, none holding the whole story
- Name, date of birth, and history re-entered at each new provider
- Labs and notes that may never reach the next visit
- Independent and solo practices with no shared system to plug into

WITH CAREMANAGER

- One health record the patient builds and owns
- A profile and history that travels with them, provider to provider
- Independent, alternative-care providers able to attach to it
- A clean patient experience on mobile and web from day one

04 What we would build

Each part of the platform, with a one-line description of what it does.

Identity & Family Circle

Sign-up, sign-in, profile switching, and secure data sharing, so a patient can manage their own record and the records of the people in their care.

Personal Health Record

A complete record — insurance, care team, medications, allergies, vaccinations, history, surgeries, visits, labs, imaging, hospitalizations, devices, and more — each with its own structured entry and document attachments.

Care Coordination

Tasks, appointments, a document inbox, and notifications that keep a patient on top of their own care, across every provider they see.

Mobile Experience

A native iOS and Android app with the full record, camera-based document capture, and Apple Health / Google Fit integration.

Platform Operations

The super admin console — client accounts, dashboards, and the configuration library the operations team runs the platform from.

Security & Compliance Foundation

Multi-tenant identity, encrypted storage, malware-scanned uploads, and a HIPAA-ready environment underneath every screen.


05 How the pieces connect

A patient's record, and how each role reaches it.

A patient signs up once and builds a record that lives entirely inside CareManager, not inside any single clinic's system. They can add family members or invited caregivers with their own access, and share select parts of their record with a provider, one visit at a time. The Super Admin platform sits above this as the operational layer — provisioning accounts, watching platform health, and managing the configuration every patient-facing screen reads from.


This first build does not yet include a dedicated workspace for providers themselves — the record is structured to make that a clean next step, not a rebuild.

 Patient-owned  Platform-operated

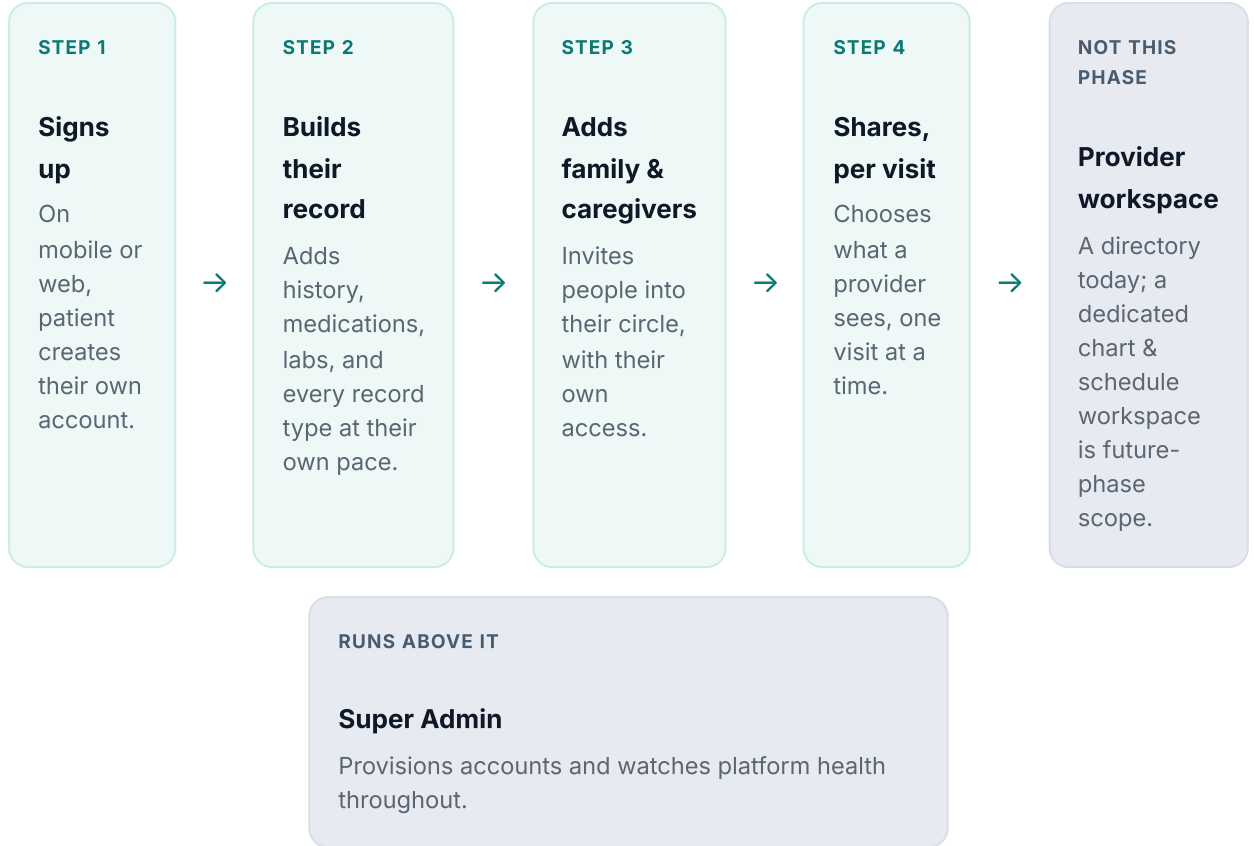

06 Architecture and integrations

A modern, typed stack, with identity and payments handled by proven services.

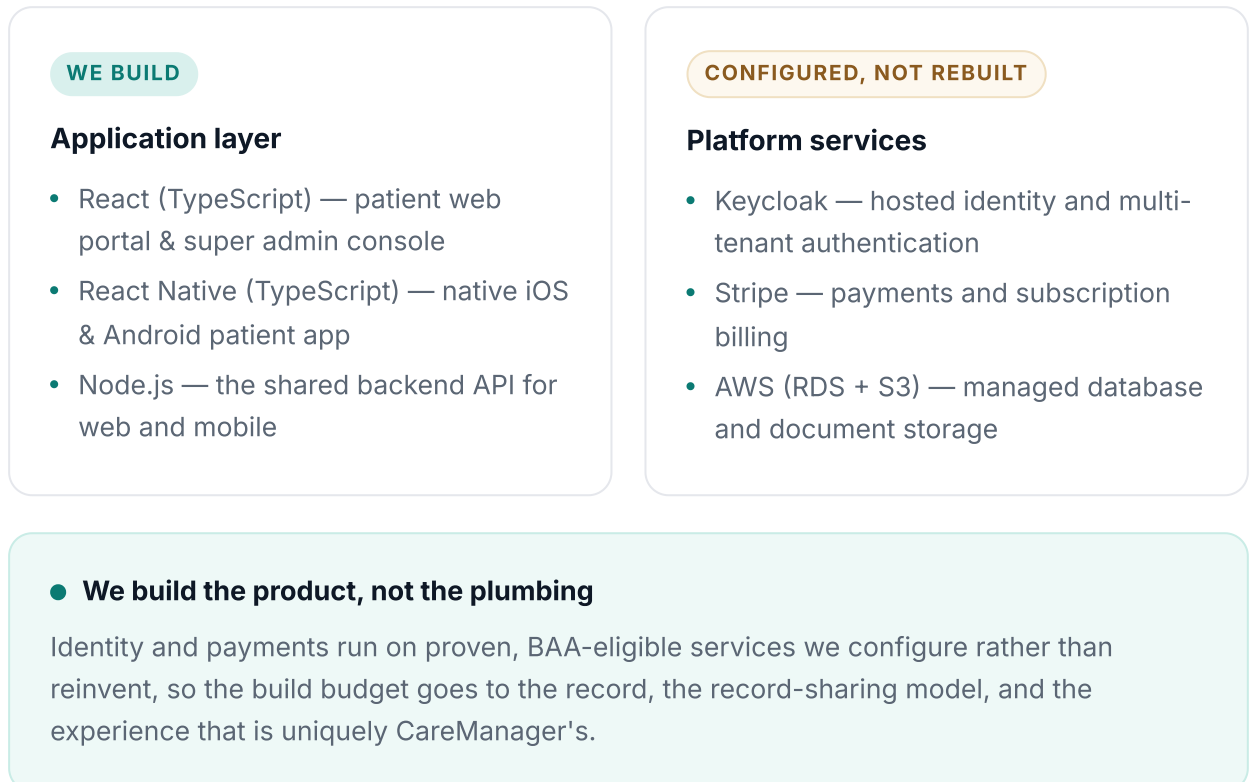

07 Security, compliance and ownership

Built HIPAA-ready from the first environment; certification is a process you own, and we help you run it.

What CareManager protects

- Encryption in transit and at rest
- Malware-scanned document uploads (Yara + ClamAV)
- Multi-tenant identity isolation via Keycloak
- Audit logging across the platform

What you own

- Full code ownership, IP assigned on delivery
- Infrastructure in your own cloud account
- A patient's data belongs to their record — not to any single clinic

● HIPAA-ready vs. HIPAA-certified

We build CareManager's platform and architecture to be **HIPAA-ready** — encryption, access controls, audit logging, and the infrastructure patterns HIPAA expects, in place from the first environment. Formal HIPAA **certification** is a compliance process CareManager itself has to complete, typically by subscribing to a compliance-automation service such as Sprinto or similar, alongside a third-party audit. Mindbowser is not the certifying party, but we help: preparing the technical evidence, closing any gaps a compliance review surfaces, and supporting the audit itself.

Mindbowser separately holds its own SOC 2 Type II certification as a company (see About Mindbowser) — that is Mindbowser's own credential, distinct from CareManager's own compliance certification, which remains yours to obtain.

08 DevOps and environments

Security and testing automated into the pipeline, not bolted on at the end.



Infrastructure as code

OpenTofu + Terragrunt across Dev, QA, Stage, and a HIPAA-ready single-AZ production environment.

Delivery pipelines

CI/CD for the web app, the backend, and mobile app builds and store publishing (Android and iOS).

Security gates

File-scanning on every upload (Yara + ClamAV), cloud posture scanning (Prowler), and a pentesting pass before go-live.

Multi-tenant identity

Keycloak configured with organization support, so multi-tenancy is foundational, not retrofitted.

● DevOps splits across both phases

Phase 1 stands up the full HIPAA-ready foundation above: a single-AZ production environment, CI/CD, multi-tenant identity, and the security gates. **Multi-AZ resilience and disaster-recovery setup are Phase 2 scope** — see section 10 — once real usage patterns inform how the platform should scale.

09 Phase 1 scope, by role

Everything a patient needs to build their record, and the platform behind it.

PATIENT — WEB

- **Identity & profiles:** sign-up/in, verification, password reset, Google/Apple sign-in, profile switching for family members
- **Data sharing & caregiving:** share your record, see what's shared with you, manage caregiving requests
- **Personal health record:** insurance, care team directory, medications & supplements, allergies, vaccinations, medical/family/social history, life events, surgeries, office visits, laboratory, imaging, hospitalizations, other procedures & documents, medical devices, behavioral health, and medical aesthetics — each with document attachments
- **Care coordination:** dashboard, tasks, appointments, document inbox, notifications
- **Account tools:** settings, help center, PDF/CSV export of any record

PATIENT — MOBILE (IOS & ANDROID)

- Full parity with the web record, built native
- Camera and file capture for documents, on every record type
- Apple Health / Google Fit connections
- Push notifications, and the same family/caregiving model as web

SUPER ADMIN — WEB

- Platform dashboard: growth and engagement metrics
- Client account management, with a full audit trail
- Configuration library: dropdown option lists, help center FAQs, legal document metadata, reminder templates
- Notifications and settings

DEVOPS / PLATFORM

- HIPAA-ready environments (Dev, QA, UAT, Prod), infrastructure as code, single-AZ production
- CI/CD for web, backend, and mobile releases
- Multi-tenant identity, file-scanning, cloud security posture, and a pre-launch pentest pass
- Multi-AZ resilience and disaster-recovery are Phase 2 scope

- **Noted for later, not built in Phase 1 or 2**

A dedicated **Care Coordinator (CSM)** role is intentionally out of scope for both phases. It's recommended for a future phase, once real Phase 1 usage shows what the coordinator's permissions and workflows actually need to be — that avoids designing it twice.

10 Phase 2, at a glance

Kept brief by design — full scope is defined once Phase 1 is underway.

Phase 2 builds the engagement layer and platform monetization on top of Phase 1, and continues DevOps into production resilience. It isn't broken out milestone-by-milestone here — that detail follows once Phase 1 scope is locked and real usage starts informing it.

Patient engagement

Insights, goals, resources, journals, and events & programs — the layer that keeps people coming back once the core record is in daily use.

Monetization & admin

Subscription plans & services, Stripe-synced billing visibility, and platform users (sub-admin accounts) for the operations team.

Production resilience (DevOps)

Multi-AZ infrastructure, disaster-recovery setup and drills, and ongoing infra optimization as real traffic arrives.

~1.5 mo

Indicative Phase 2 duration

USD 42,868

Indicative Phase 2 investment

Indicative only — not part of this proposal's milestone plan or Phase 1 total. Firmed up in its own scoping pass once Phase 1 is underway.

11 Delivery approach and milestones

Two-week milestones, each a demonstrable release you sign off before the next begins.

This is a tentative, planning-grade shape rather than a set of hour estimates — a way to reason about sequence and cash flow together. Each milestone is two weeks, gated on your acceptance, and tied to a payment tranche.

- **Indicative, confirmed at M0**

The milestones and sequence below are indicative for planning purposes. We review and firm them up together at Kickoff & Planning (M0), and share the updated plan once the architecture and scope are locked.

Phase 1

M0

M1

M2

M3

M4

M5

M6

M7

M8

 Phase 1 milestone (2 wks each)

Phase 1 milestones

 Kickoff & Planning M0 · 2 wks · 20%

Project setup, account provisioning, database and architecture design.

 Foundations M1 · 2 wks · 10%

Identity, profiles, and the data-sharing / caregiving model.

 Health Record I M2 · 2 wks · 10%

Dashboard, plus the first wave of record modules: insurance, care team, medications, allergies, vaccinations, and history.

 Health Record II M3 · 2 wks · 10%

The remaining record modules — surgeries, visits, labs, imaging, hospitalizations, devices, and more — plus PDF/CSV export.

 Mobile Experience M4 · 2 wks · 10%

The native iOS and Android app, camera capture, and Apple Health / Google Fit.

 Care Coordination M5 · 2 wks · 10%

Tasks, appointments, document inbox, and notifications.

 Super Admin M6 · 2 wks · 10%

Platform dashboard, client accounts, and the configuration library.

 Platform Hardening M7 · 2 wks · 10%

Multi-tenant identity, file-scanning, cloud security posture, and the pre-launch pentest pass.

 UAT & Go-live M8 · 2 wks · 10%

End-to-end testing, your sign-off, and delivery.

 On timing

Durations above are a tentative, two-week-sprint shape for planning — nine milestones for Phase 1, roughly 4 to 4.5 months. Firm calendar dates are confirmed once the team is mobilized at M0.

12 How we work together

One transparent process, so you always know where things stand.

Our team tracks the work internally in Jira, with code in Git under pull-request review. You get a clear window into it through weekly status reports and a shared Slack channel for fast, day-to-day back-and-forth.

Jira

Our internal sprint board: stories, tasks, and progress across two-week milestones.

Slack

A shared channel for fast questions and quick decisions, with daily timezone overlap.

Git

Version control with pull requests and code review, and full IP assignment to you on delivery.

The cadence

● Every day **SLACK + ASYNC STANDUP**

Fast questions and quick decisions in a shared channel, with daily overlap in your timezone.

● Every week **STATUS + LIVE DEMO**

A weekly status report and a live demo against the milestone in progress.

● Every milestone **RELEASE + YOUR SIGN-OFF**

A demonstrable release, then your acceptance before the next milestone begins.

● Delivery

Production cutover, coordinated closely with your team.

● Complimentary support · 1 month **BUG FIXES**

One month of complimentary issue and bug-fix support after delivery, on UAT or an equivalent environment, before a paid maintenance plan takes over.

13 Indicative plan: duration and investment

A phased shape you can plan around.




Where the effort concentrates

- **Largest:** the personal health record, across web and native mobile
- **Moderate:** care coordination, admin operations, and the security/DevOps foundation

Phase 1 is **USD 135,057**, delivered across nine two-week milestones — Kickoff at 20%, and each remaining milestone released at 10% on your acceptance. This is Phase 1 only; Phase 2's indicative timeline and cost are covered separately in section 10 and are not part of this total.

Phase 1 — payment by milestone

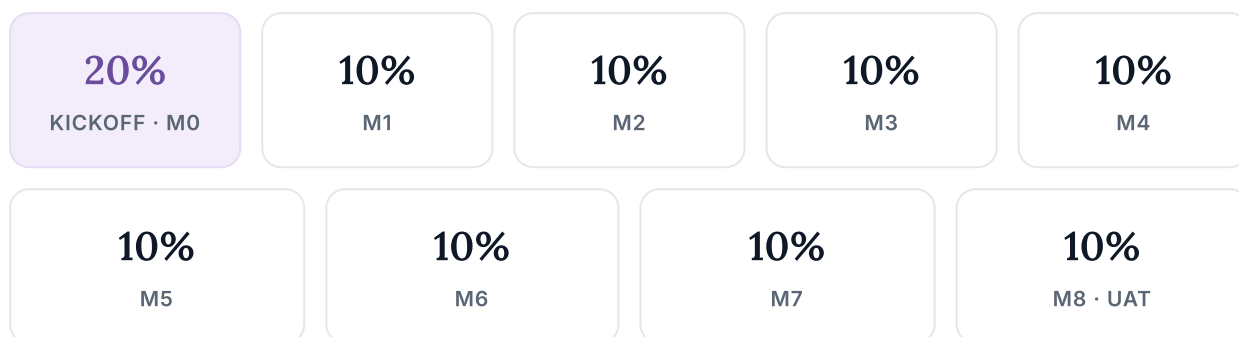

Fixed-fee, each tranche released on your acceptance. Milestones are indicative and confirmed at M0 (see section 11).

14 After launch and the partnership

The relationship doesn't end at go-live; it's where the partnership starts to compound.

Support after delivery

1 month, complimentary

One month of complimentary support for issues and bug fixes after delivery, on UAT or an equivalent environment — no charge.

Paid maintenance & support

After the complimentary month, a paid maintenance and support plan keeps the platform running — monitoring, fixes, and small iterations. **[[TO CONFIRM: plan and pricing]]**

Clean handover

Runbooks, a recorded handover, and code in your accounts, so your team can operate it independently.

The partnership advantage

Healthcare playbook

The best practices we've learned across many US healthcare launches, applied to CareManager's record and onboarding.

Expert working sessions

Sessions with our clinical and interoperability SMEs to sharpen the record model as real providers connect.

Built to scale

Engineered to grow with your patient volume without a rebuild, so the same team can carry the provider workspace and expansion goals forward.

15 Risks, and how we handle them

Named up front, with a plan already attached.

RISK

HOW WE HANDLE IT

Broad record scope

Nineteen-plus record modules ship inside a milestone-gated build; nothing merges without your sign-off, so the surface stays manageable one milestone at a time.

Multi-tenant identity from day one

Keycloak's organization support is configured in the Foundations milestone, before any patient-facing screen depends on it.

Native mobile app store review

iOS and Android submissions begin as soon as builds are stable, so review time doesn't sit on the critical path at the end.

The independent-provider model is new

Phase 1 and 2 ship the patient side first; the provider workspace is a deliberate next-phase scope, not something improvised inside this build.

Scope creep across many record types

Milestones are acceptance-gated — launch-critical modules first, the rest as an agreed fast-follow.

16 The team and next steps

A small, senior team, on it start to finish.

One accountable lead owns delivery, with daily overlap and a live demo each week.

Personal health record platforms

HIPAA-ready engineering

React & React Native

Multi-tenant identity (Keycloak)

Engagement lead and architect

Owens delivery, the architecture, and the client relationship.

Senior full-stack engineers

Web, mobile, and backend, with QA alongside them.

DevOps & security engineer

Infrastructure, CI/CD, and the compliance posture.

A business analyst front-loads Kickoff & Planning; DevOps and QA run shared across the build. Named individuals and bios come with the signed proposal, along with the firm plan.

The natural next step is a kickoff working session, where we confirm the architecture together and lock the Milestone 0 plan.
